

Sidewalk Project Plan and Progress

Began with 1,471 locations from 311 request backlog (received prior to December 31, 2016).


Full block inspections have been done for approximately 75% of the locations, and identified two types of conditions:

- Blocks where spot repair would be pursued for the full block due to overall good or fair conditions
- Blocks where full replacement is recommended in the future due to overall poor condition

The City issued an RFP for inspections to assist in completing the systematic inspections and is pursuing contracts with three engineering design firms.

Blocks identified for sidewalk repair through 311 request backlog

■ Project underway ■ Future projects

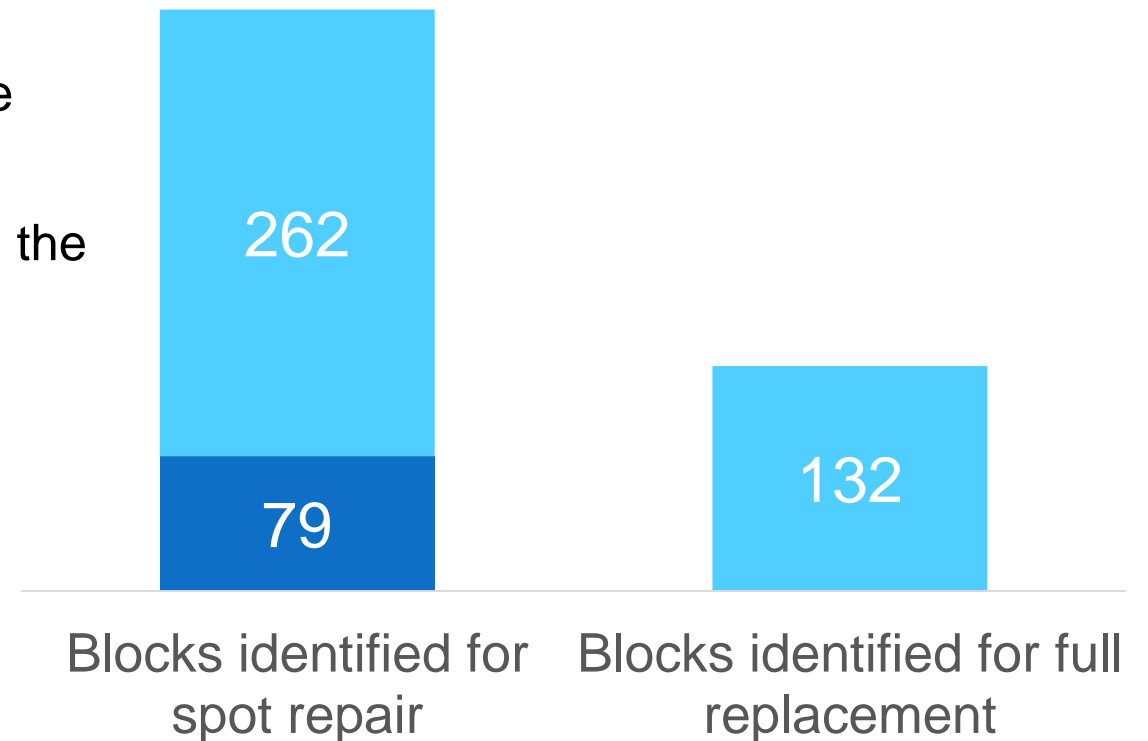

CITY OF
KANSAS CITY,
MISSOURI

Curb Ramps

Projects Underway

- **117 corners** were completed by March 2018
- **120 corners** began in August 2018

Remaining Volume

- **1,830 unramped corners** remain to be reconstructed
- Estimated timeframe for completion is 4 years

Sidewalk Repair Requests

	Backlog Requests (Prior to 12/31/16)	Spot Repair - Blocks Underway (Year 1 GO Bond)	Spot Repair - Blocks Remaining	Blocks Identified for Future Replacement
North of the river	232		111	11
River to 39 th Street	502	32	38	67
39 th Street to 85 th Street	653	47	74	52
South of 85 th Street	84		39	2

